"2nd & final Bill"

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486601

Serial No. .....

Name of work ..... From ..... To SBRW/30/20-4

Name of Contractor of nature of Agency..... D: 31/5/2020

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of Work :- Improvement and Asphalting to Sapthagiri College Main Road and adjacent cross roads in Ward No. 12, Shettyhalli, Sulebhavan.						
	Estimated Cost :- Rs. 200.00 Lakhs.						
	Job Code No. :- 012-19-000053.						
	Admin Approval :-	NO/BBMP/EE/DD/AS/	173/2018-19 dtd. 20-02-19				
	Technical Sanction :-	No./BBMP/CE/DB/	TS/191/2018-19 dtd. 22.02.19				
	Contractor :- M/S KRIDL, B'lore						

"COST ABSTRACTS"

MEASUREMENT BOOK

Date	Full description, etc, of work		Dimensions				Contents		Reference to last Measurement	
			Number	Length	Breadth	Depth				
1	2		3	4	5	6	7		8	
			Previous			Present			up to date	
Sl. No.	Description of Work,	Unit	Qty.	Amounts	Qty	Rate	Amounts		Qty	Amount
1	EWE for Drain.	Cum	1352.16	298016.06	0	220.40	0.00		1352.16	298016.06
2	PCC 1:3:6. Concrete	Cum	220.19	11938468.16	0	5421.50	0.00		220.19	11938468.16
3	RCC M20 Concrete	Cum	395.42	279568848	0	7070.20	0.00		395.42	279568848
4	TMT steel.	MT	29.66	2145218.23	0	72326.78	0.00		29.66	2145218.23
5	CC 1:2:4 Coverslab	Sqm	1106.10	2442268.80	0	2208.00	0.00		1106.10	2442268.8
6	EWE for Road work	Cum	1421.27	98152.91	0	69.06	0.00		1421.27	98152.91
7	OGL Compaction	Sqm	5685.08	36157.11	0	6.36	0.00		5685.08	36157.11
8	GSB,	Cum	852.76	17011879.8	0	19949.2	0.00		852.76	17011879.8
9	WMM,	Cum	1279.14	25599173.30	0	20012.8	0.00		1279.14	25599173.3
10	Primer Coat	Sqm	0	0	5685.08	29.68	168733.03		5685.08	168733.03
11	Tack Coat	Sqm	0	0	5685.08	12.72	72314.15		5685.08	72314.15

Audited and admitted for Rs. 4213250=00

Passed by Cheque for Rs. 3649728=00

(Serial No.

Name of work

Name of Contractor of nature of Agency

Date of commencement of work

Accounts Superintendent Exe. Engineer

Dept. B.B.M.P. Dasarahalli Division

KRIDL 4%.

M. A. R. 57 (Rule 116) No. E 486602

Measurement Book

From

To

Goods - 4128814 - Ded - 479086 - Net - 3649728

	Full description, etc. of work		Number	Dimensions: Length	Breadth	Depth	Contents	Reference to last Measurement
1	2		3	4	5	6		
12	DBM.	Cum	0	0.0	284.25	6858.20	1949469.07	284.25
13	BC.	Cum	0	0.0	170.55	7911.84	1349382.11	170.55
14	Thermoplastic Rolling	Sqm	0	0.0	168.60	456.74	76669.16	168.60
	Total						3616567.53	
	GST 12%						433988.10	
	KRIDL 4.5%						162745.54	
	Grand Total						4213301.17	

1949469.07 = 00

1689427.5 = 1689427699 Total 3616523

1592.455 = 20273313.24 433983

597.171 = 7602426.66 162744

19681832.69

16881830=00

1546008.9=00

4213250=00 19673339=00

ಸಹಾಯಕ ಅಧೀಕ್ಷಕ ಅಭಿಯಂತರರು ಅಭಿಯಂತರರು
ಶಿವಪ್ಪಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Name of Work;- Improvements and Asphalting to Sapthagiri College Main and adjacent cross roads in ward no. 12. Shettyhalli Sub division

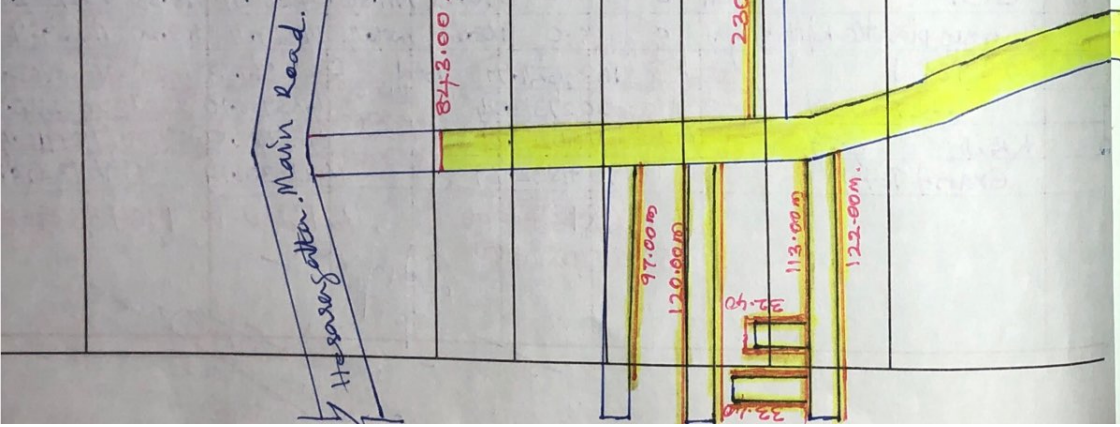

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486603

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

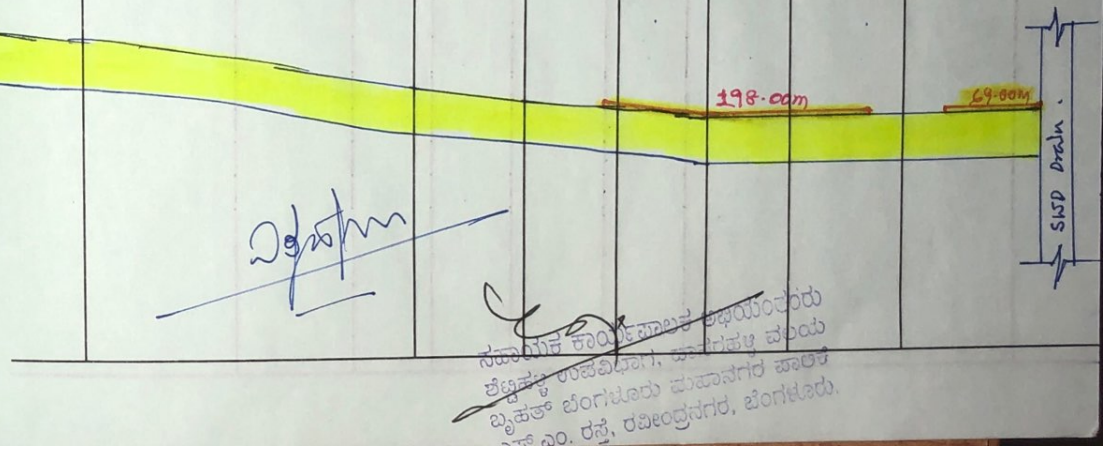

ನಕಾಯಿಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಪೆಟ್ಟಣಕ್ಕೆ ಉಪವಿಭಾಗ, ಮಾದಾವರ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.
